


Axom Adarxo Gram Yoiona

Name of LAC	Name of Village	Number of Schemes Taken up	Fund Received	Schematic Value	Amount Utilised	Remarks
Dhubri LAC	Madhusoulmari Pt.I	6	5000000.00	4974320.00	4974320.00	Work in progress. CC, Photograph not yet received form the VLCC.
	Kismat Hasdaha Pt.II	6	5000000.00	4989220.00	4989220.00	
Gauripur LAC	Madaikhali	4	5000000.00	4950000.00	4950000.00	Work in progress. CC, Photograph not yet received form the VLCC.
	Debottar Barundanga	5	5000000.00	5000000.00	5000000.00	
Golakganj LAC	Bishkhowa Pt.IV	5	5000000.00	5000000.00	5000000.00	Work in progress. CC, Photograph not yet received form the VLCC.
	Jinkata Pt.II	5	5000000.00	5000000.00	5000000.00	
Bilasipara East	Barunitara Pt.II	9	5000000.00	5000000.00	5000000.00	Completed
	Sasargaon Pt.II	3	5000000.00	5000000.00	5000000.00	Work in progress. CC, Photograph not yet received form the VLCC.
Bilasipara West	Ghashbari	4	5000000.00	5000000.00	5000000.00	Work in progress. CC, Photograph not yet received form the VLCC.
	Kadamtala Pt.II	4	5000000.00	5000000.00	5000000.00	Completed




**Installation of Solar Light
at Vill.-Kadamtola Pt.-II**

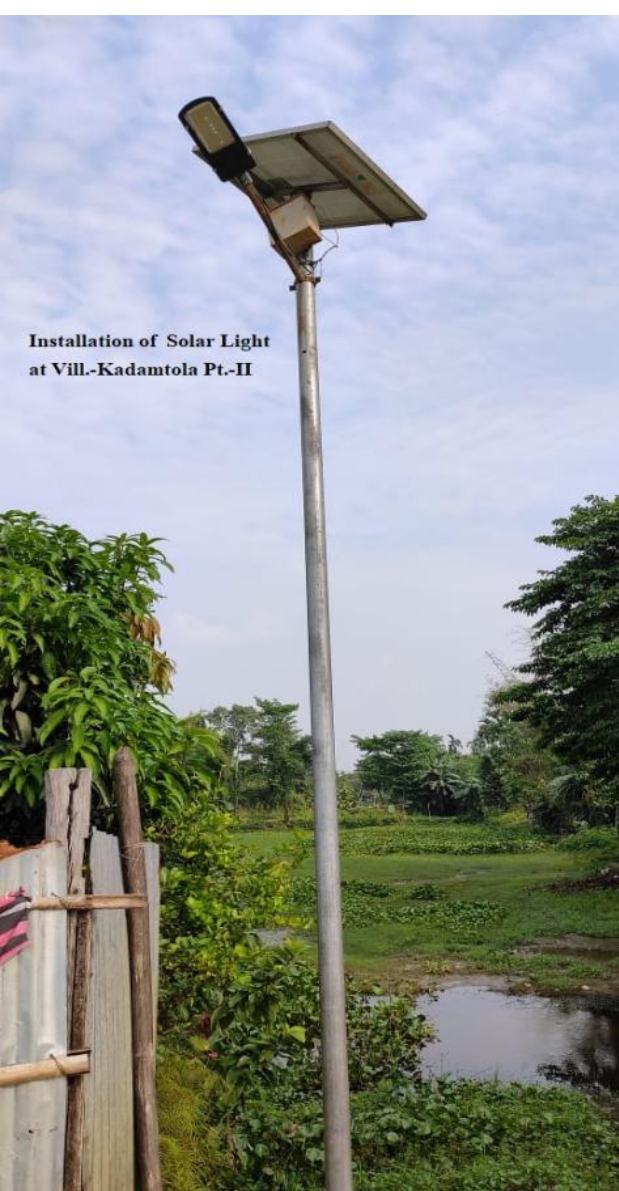

Latitude: 26.223097
Longitude: 90.216176
Elevation: 38.71 m
Accuracy: 3.8 m
Time: 14-08-2021 12:55
Note: cc block

**Construction of CC Block Road from PWD
towards Kalimandir at Vill.-Kadamtola Pt.-II**

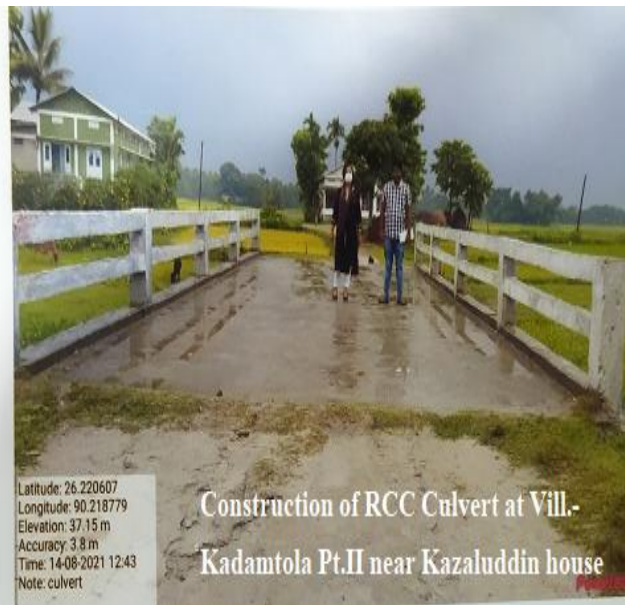


Latitude: 26.220607
Longitude: 90.218779
Elevation: 37.15 m
Accuracy: 3.8 m
Time: 14-08-2021 12:43
Note: culvert

**Construction of RCC Culvert at Vill.-
Kadamtola Pt.II near Kazaluddin house**



**Construction of CC Block Road from Fokir
Bepari house to Ohed Bepari house at Vill.-
Kadamtola Pt.-II**

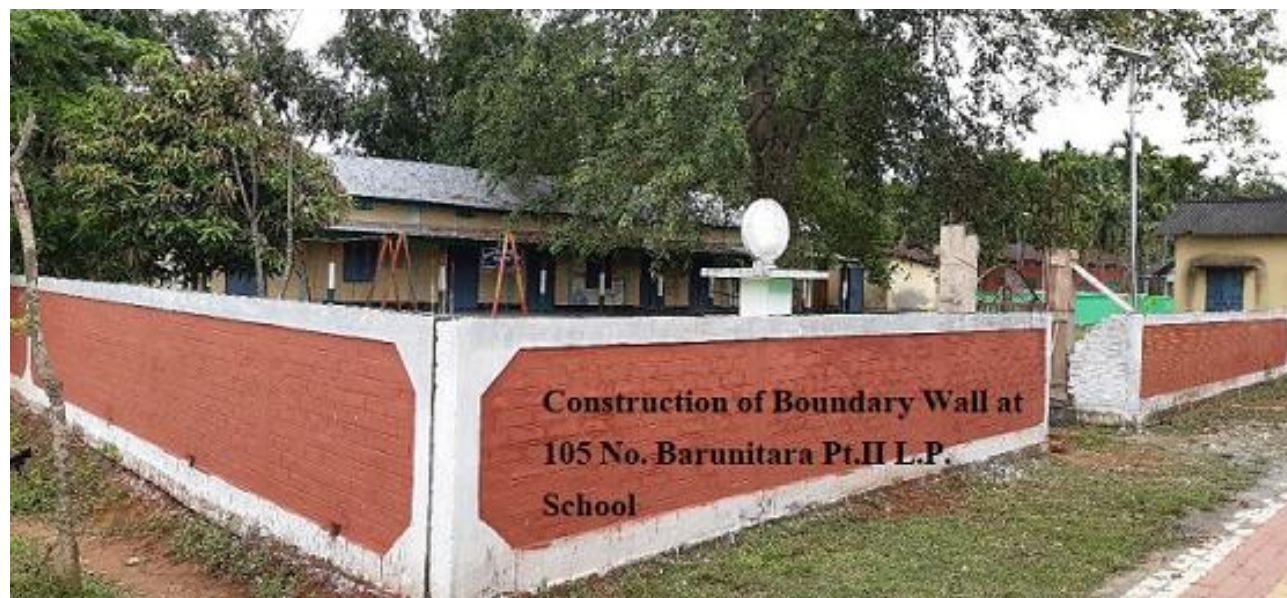

**Construction of Boundary Wall at
105 No. Barunitara Pt.II L.P.
School**



**Installation of Solar Street
Light at Barunitara Pt.II Road**
